

Stroom Capaciteitsrapport

PQBOX150 V4.614

Gegenereerd: 16 Mar 2026 15:54

Analyseperiode	Maximale stroom (ingesteld)	Aantal fasen
9/12/2025 08:00 -> 11/12/2025 07:20	63 A	4


Resultaten per fase

Fase	Gem. (A)	Gem. (%)	Piek (A)	Piek (%)	Ruimte gem.	Ruimte piek	Status
L1	29.3	46%	79.1	126%	+33.7 A	-16.1 A	Kritiek
L2	28.5	45%	76.0	121%	+34.5 A	-13.0 A	Kritiek
L3	28.8	46%	79.8	127%	+34.2 A	-16.8 A	Kritiek
N	9.0	14%	17.4	28%	+54.0 A	+45.6 A	OK

Bezettingsgrafiek

L1		gem. 29.3 A (46%) A (126%)	piek 79.1 A	Kritiek
L2		gem. 28.5 A (45%) A (121%)	piek 76.0 A	Kritiek
L3		gem. 28.8 A (46%) A (127%)	piek 79.8 A	Kritiek
N		gem. 9.0 A (14%) A (28%)	piek 17.4 A	OK

Stroom over tijd

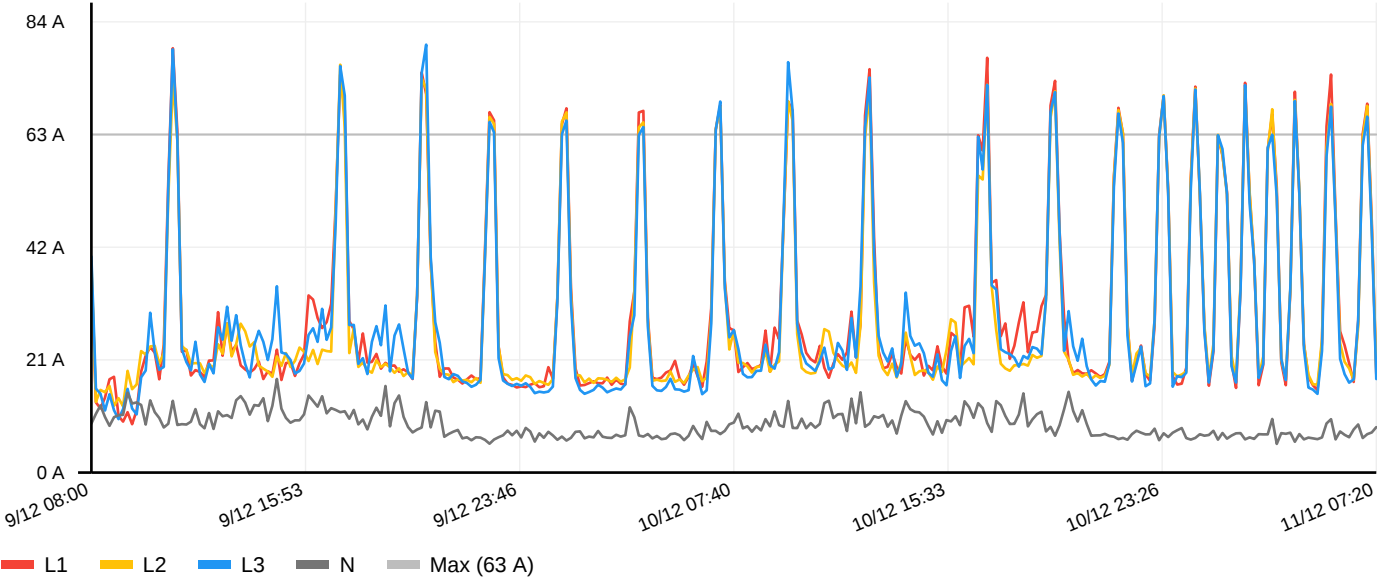

Status:	OK (piek < 70%)	Let op (70 - 90%)	Kritiek (>= 90%)	De piekstroom bepaalt de status.
---------	-----------------	-------------------	------------------	----------------------------------
